


ID	Task Name	Duration	Start	Finish	Prede	27 Sep '10							4 Oct '10							
						S	S	M	T	W	T	F	S	S	M	T	W	T	F	
1	<b>Projekt Tréner mentálnych schopností</b>	<b>70 days?</b>	<b>Mon 27.9.10</b>	<b>Thu 16.12.10</b>																
2	<b>Úvod</b>	<b>6 days?</b>	<b>Mon 27.9.10</b>	<b>Sat 2.10.10</b>																
3	Inicializácia projektu	1 day?	Mon 27.9.10	Mon 27.9.10																
4	Zadefinovanie úloh v tíme	1 day?	Tue 28.9.10	Tue 28.9.10	3															
5	Zvolenie metódy vývoja	2 days?	Wed 29.9.10	Thu 30.9.10	4															
6	Motivácia a ciele projektu	2 days?	Fri 1.10.10	Sat 2.10.10	5															
7	<b>Analýza</b>	<b>16 days?</b>	<b>Mon 4.10.10</b>	<b>Thu 21.10.10</b>	2															
8	<b>Analýza problémovej oblasti</b>	<b>6 days?</b>	<b>Mon 4.10.10</b>	<b>Sat 9.10.10</b>																
9	Štúdium problémovej oblasti	2 days?	Mon 4.10.10	Tue 5.10.10	6															
10	Finalizácia problémovej oblasti	4 days?	Wed 6.10.10	Sat 9.10.10	9															
11	<b>Analýza existujúcich riešení</b>	<b>6 days?</b>	<b>Mon 4.10.10</b>	<b>Sat 9.10.10</b>																
12	Zhodnotenie existujúcich riešení	2 days?	Mon 4.10.10	Tue 5.10.10	6															
13	Finalizácia analýzy existujúcich riešení	3 days?	Thu 7.10.10	Sat 9.10.10	12															
14	<b>Analýza požiadaviek</b>	<b>6 days?</b>	<b>Mon 4.10.10</b>	<b>Sat 9.10.10</b>																
15	Získanie a určenie požiadaviek	2 days?	Mon 4.10.10	Tue 5.10.10	6															
16	Finalizácia požiadaviek	4 days?	Wed 6.10.10	Sat 9.10.10	15															
17	<b>Analýza technológií</b>	<b>10 days?</b>	<b>Mon 11.10.10</b>	<b>Thu 21.10.10</b>																
18	Analýza platformy	2 days?	Mon 11.10.10	Tue 12.10.10	14;16															
19	Analýza technológií - architektúra	6 days?	Wed 13.10.10	Tue 19.10.10	18															
20	Analýza technológií - splnenie požiadaviek	6 days?	Wed 13.10.10	Tue 19.10.10	18															
21	Analýza technológií - gui	6 days?	Wed 13.10.10	Tue 19.10.10	18															
22	Finalizácia analýzy technológií	2 days	Wed 20.10.10	Thu 21.10.10	18;19															
23	<b>Návrh</b>	<b>15 days?</b>	<b>Fri 22.10.10</b>	<b>Sat 6.11.10</b>	7															
29	<b>Implementácia prototypu</b>	<b>20 days?</b>	<b>Mon 8.11.10</b>	<b>Tue 30.11.10</b>	23															
32	<b>Testovanie aplikácie</b>	<b>13 days</b>	<b>Wed 1.12.10</b>	<b>Thu 16.12.10</b>	29															
35	<b>Ostatné úlohy</b>	<b>62 days?</b>	<b>Fri 1.10.10</b>	<b>Fri 10.12.10</b>																


Project: ProjektovýPlán-TrénerMentálny  
Date: Tue 26.10.10

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

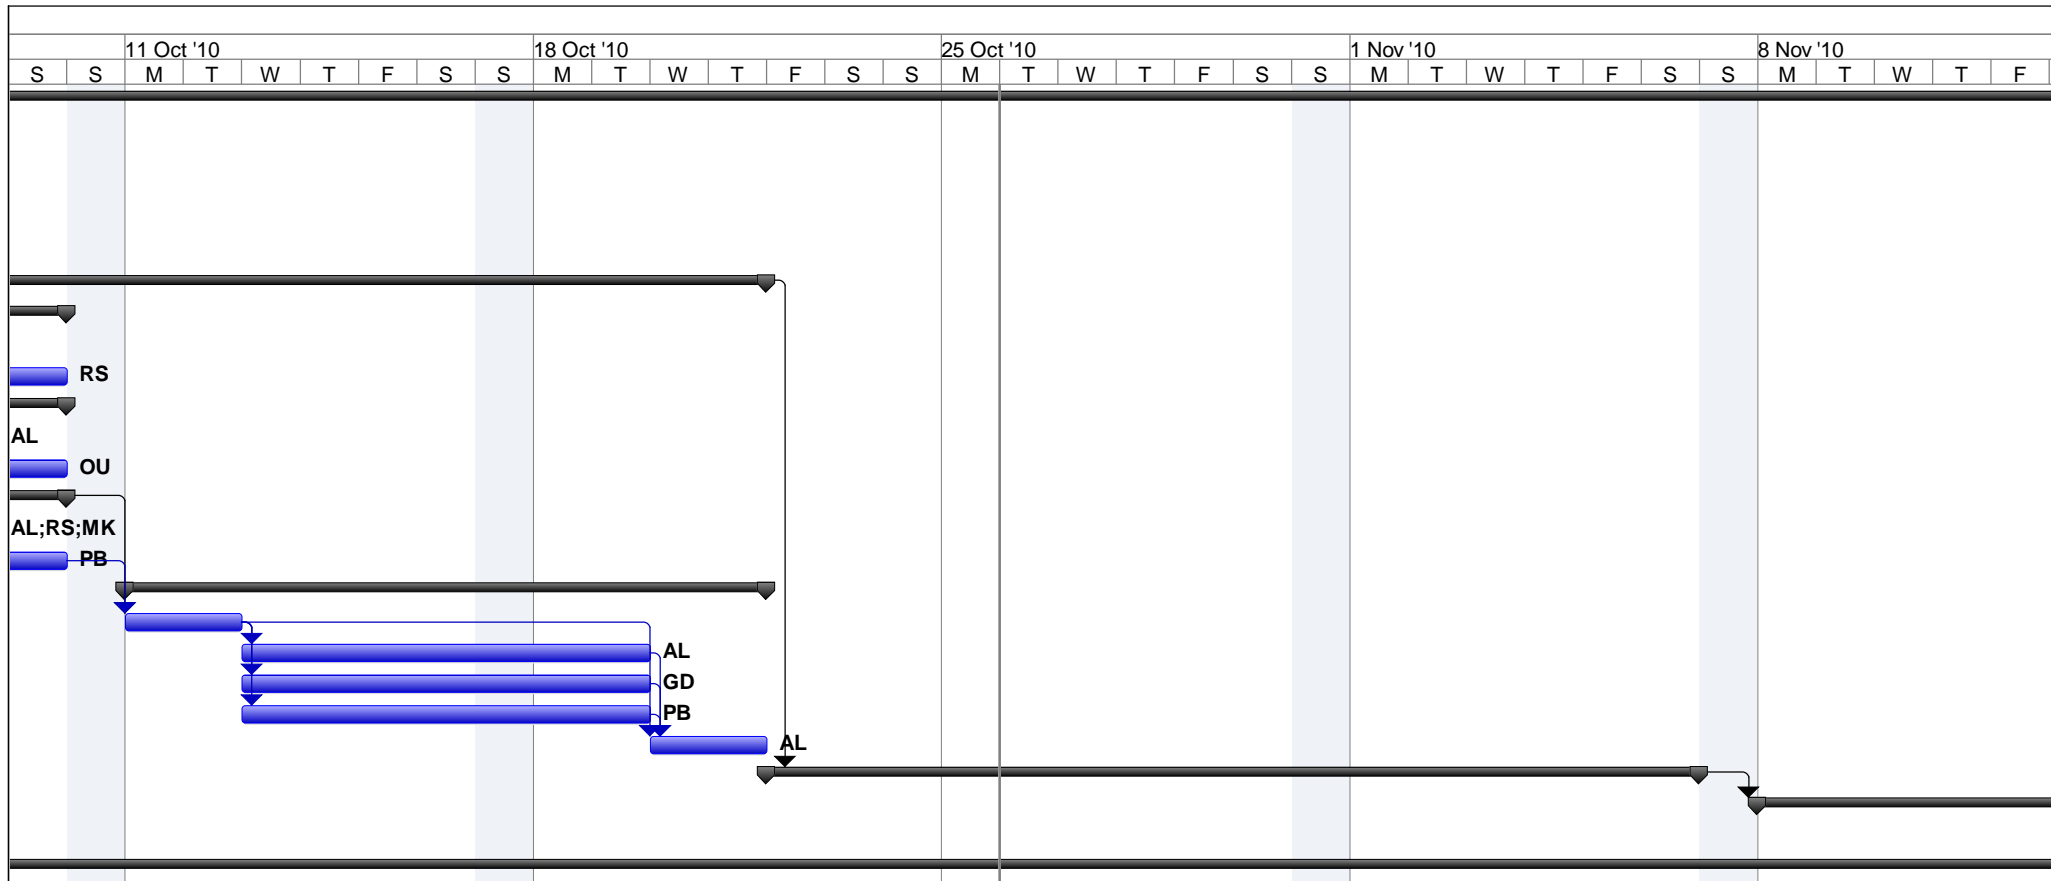

Project: ProjektovýPlán-TrénerMentálny  
Date: Tue 26.10.10

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

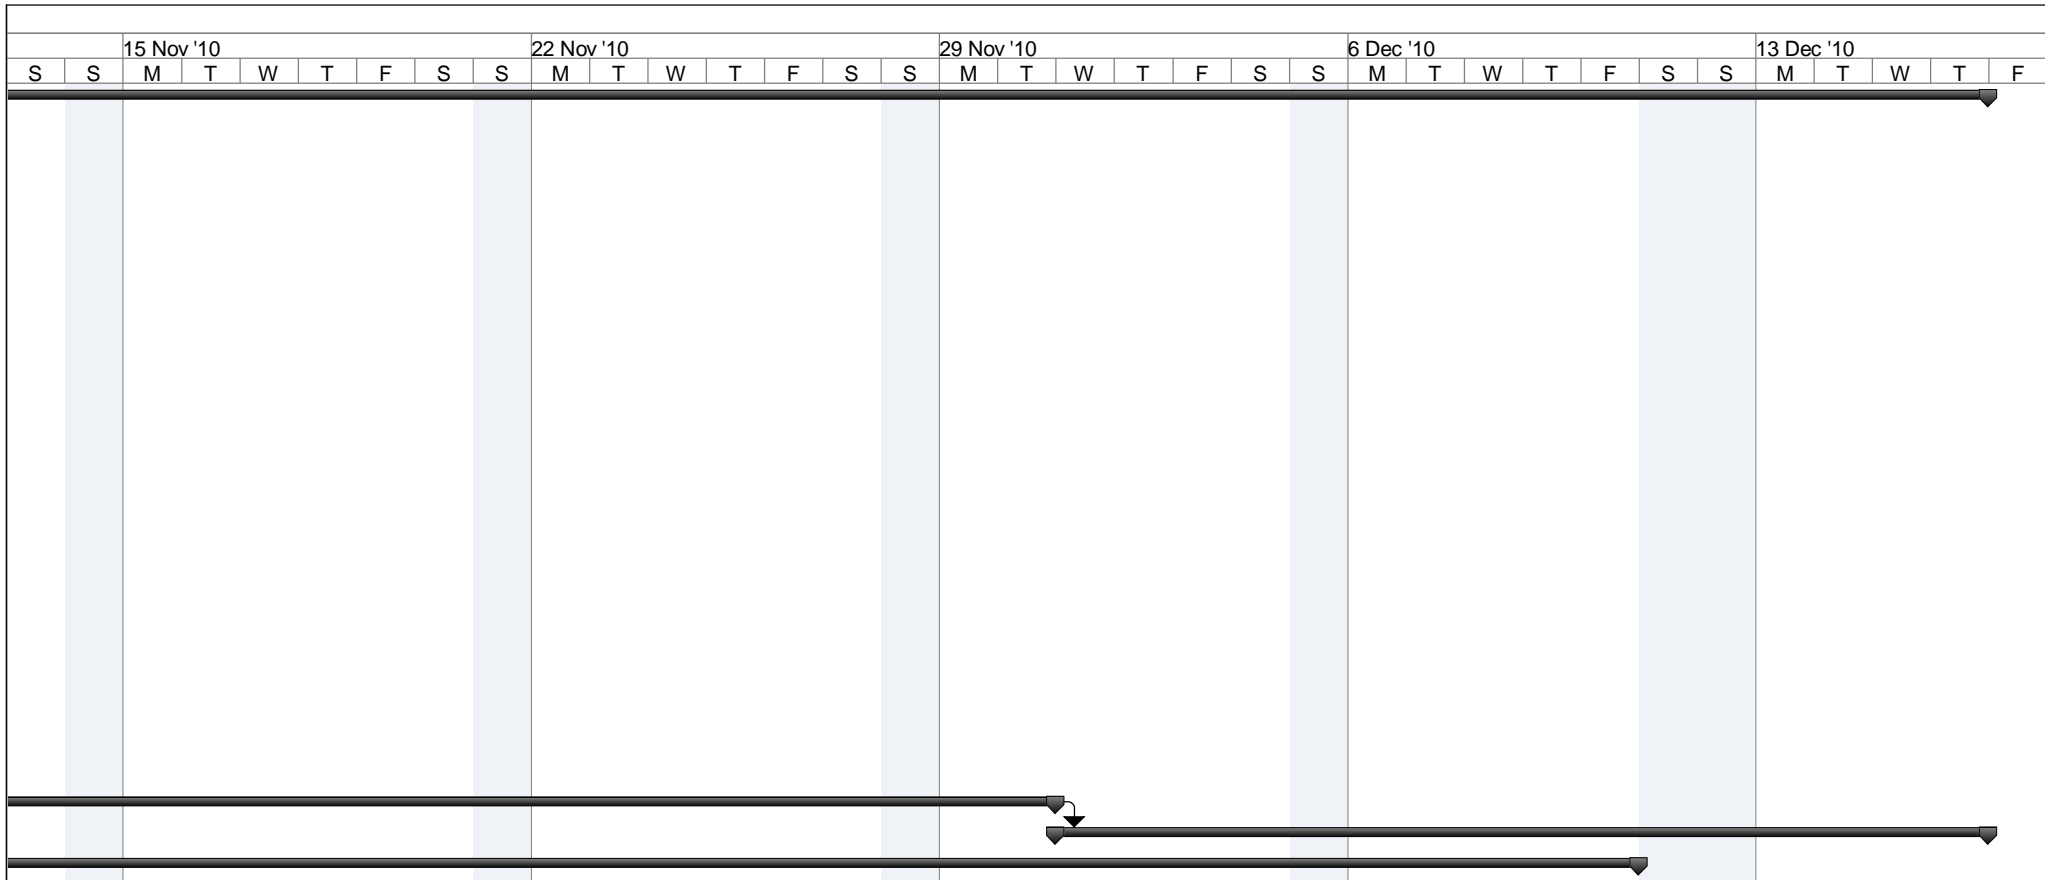

Project: ProjektovýPlán-TrénerMentálny  
Date: Tue 26.10.10

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	
